

# CHINLONE WORKPLAN



ALMA MATER STUDIORUM  
UNIVERSITÀ DI BOLOGNA



**CHINLONE Kick-off Meeting,  
Bologna 19th-21st February 2018**



Erasmus+

# PLAN OF THE PRESENTATION

## **PART 1 - GENERAL INTRODUCTION AND CONCEPTS**

- Definition of Work Packages (WP);

## **PART 2 - WORKPLAN**

- WP organization and description;
- Timeline and schedule.


# Part 1 – GENERAL INTRO AND CONCEPTS

# PROJECT STRUCTURE: The work packages (WP)

The entire project is generally divided according to **5 different stages** which cooperate to achieve the final result.

Each stage can be composed by one or more **Work Packages** with specific aims which help to better frame and organize the workflow.

Each Work Package is composed several practical **Activities**.


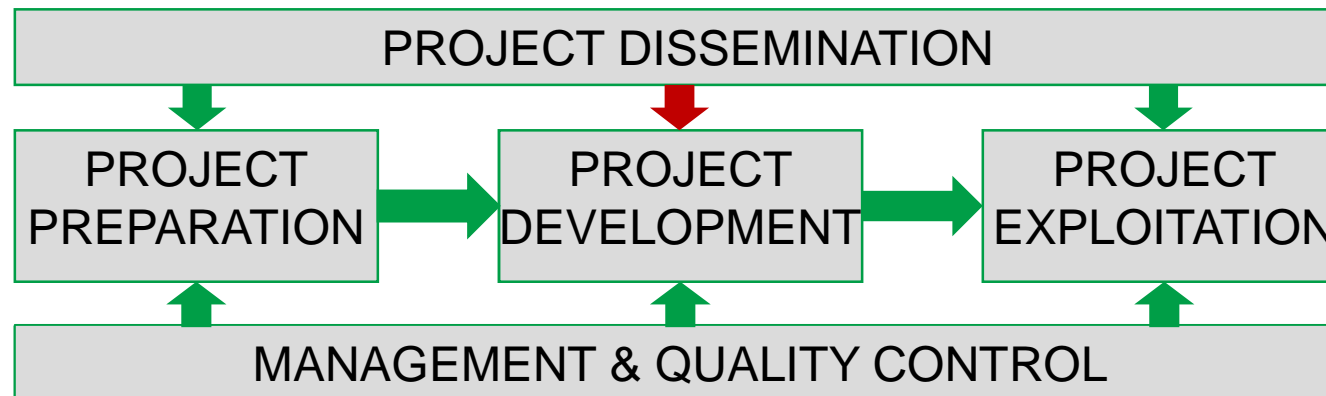


# WPs

3rd  
YEAR

2nd  
YEAR

1st  
YEAR

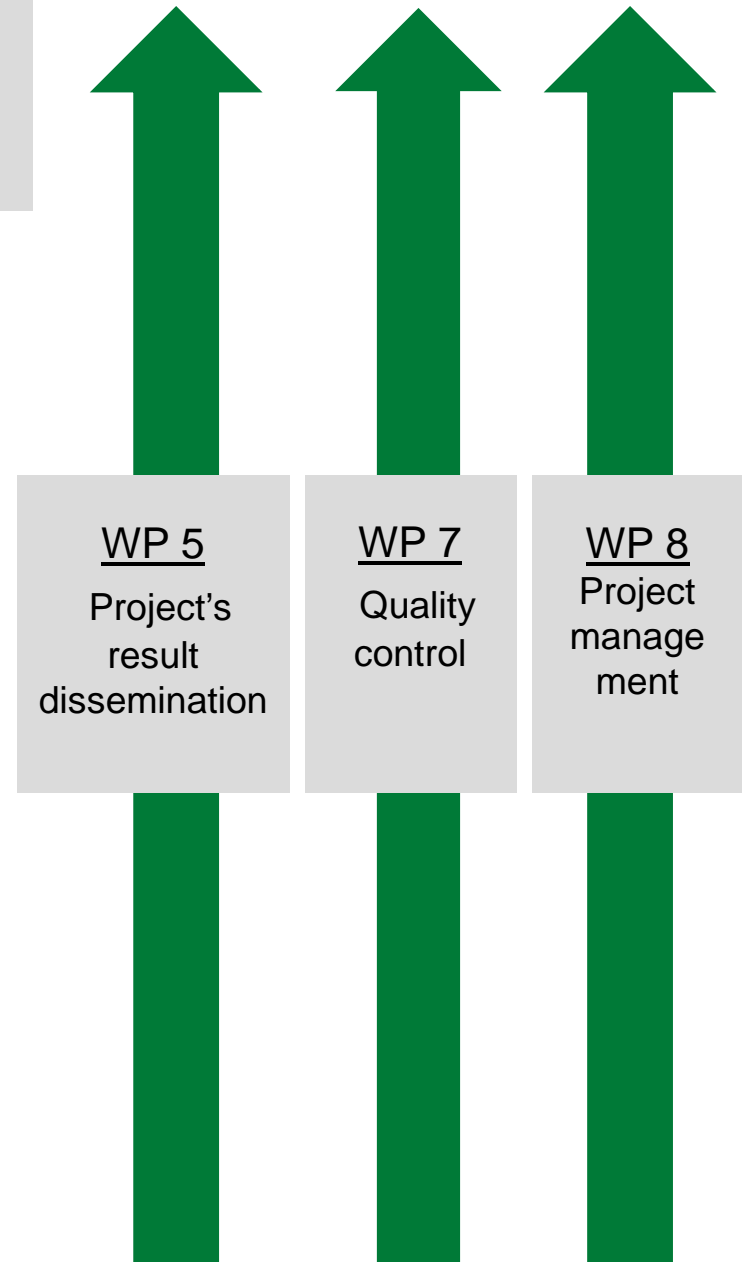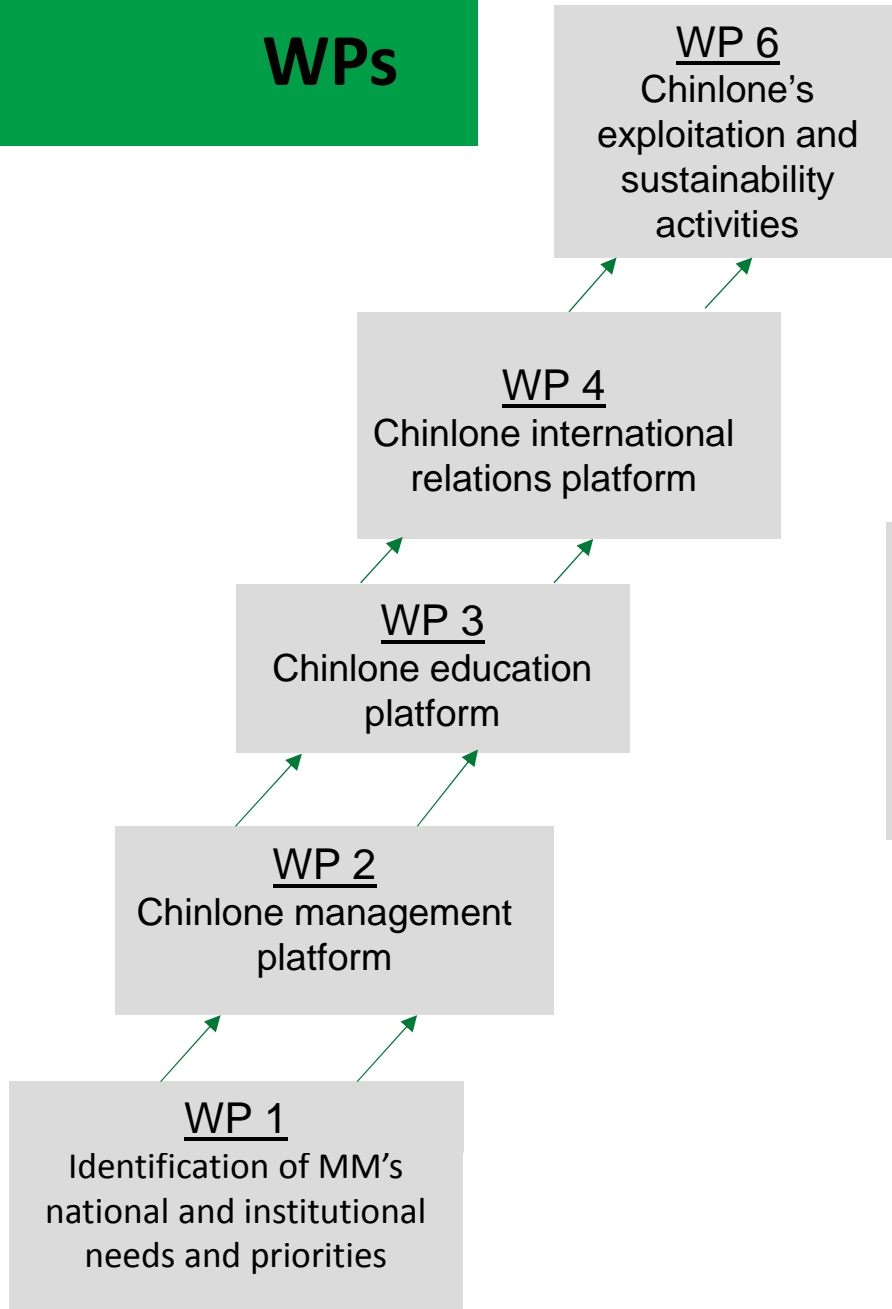

## Part 2 – WORKPLAN

# WP 1 – NEED ANALYSIS

## Timeframe - Aim - Personnel

**PERIOD:** Kick off Meeting - July 2018

**WP LEADER:** UNIBO - University of Bologna, YU - University of Yangon

**AIMS:** The primary goal in this preparatory WP is to gather all the relevant info and data on the present status of Myanmar's HES, so to acquire an accurate knowledge in terms of the latest transformations occurred, as well as regarding the national needs and priorities.

**TEAM AND PERSONNEL:** UNIBO + MM partners

# WP 1 – NEED ANALYSIS

## Activities

Activities		Personnel
No.	Title	
1	Info-collecting on current status of HES in MM	UNIBO+ MM PARTNERS
2	Needs assessment on project's target groups;	UNIBO+ MM PARTNERS
3	Drafting of MM's 'Educational Map'	UNIBO+ MM PARTNERS
4	WP outcomes shared with MM's academic community and ext. stakeholders	CONSORTIUM



## **WP 2 – CHINLONE MANAGEMENT PLATFORM**

### **Timeframe - Aim - Personnel**

**PERIOD:** September 2018 - 15 September 2019

**WP LEADER:** CG- Coimbra Group, MoE- Ministry of Education

**AIMS:** Enhancing MM University leaders' capacity in shaping and innovating university management and at supporting them in the drafting of programmatic documents such as university mission, strategic plan and international relation strategic plans.

**TEAM AND PERSONNEL:** The Consortium

# WP 2 – CHINLONE MANAGMENT PLATFORM

## Activities

Activities		Personnel
No.	Title	
1	Conference on the 'Bologna Process'	Consortium partners
2	Reviewing/Drafting and Approval of the University Mission	MM partners
3	Conference on University Leadership and Governance	Consortium partners
4	Reviewing/Drafting and Approval of the University Strategic Plan	MM partners
5	Conference on University International Dimension	Consortium partners
6	Reviewing/Drafting and Approval of the University Strategic Plan for Internationalization	MM partners
7	WP outcomes shared with Rectors of MM's central and regional HEIs	Consortium partners and representatives of MM Universities

## **WP 3 – CHINLONE EDUCATION PLATFORM**

### **Timeframe - Aim - Personnel**

**PERIOD:** January 2019 - January 2020

**WP LEADER:** UGR- University of Granada, MU- University of Mandalay

**AIMS:** restructuring and modernization of degree courses according to an approach based on students' learning outcomes. Pilot field of studies: Humanities and Cultural Heritage/Economics of Tourism/Agricultural Sciences

**TEAM AND PERSONNEL:** CHINLONE Consortium

# WP 3 – CHINLONE EDUCATION PLATFORM

## Activities

Activities		Personnel
No.	Title	
1	Identification of Task Forces members	Consortium Partners
2	Study Visits for Education Platform for Humanities and Cultural Heritage	Consortium Partners
3	Study Visits for Education Platform for Economics of Tourism	Consortium Partners
4	Study Visits for Education Platform for Agricultural Sciences	Consortium Partners
5	Cascade trainings for spill-over effect for Each Education Platform	MM partners
6	Reviewing and restructuring of course curricula	MM partners

## **WP 4 – CHINLONE IR PLATFORM**

### **Timeframe - Aim - Personnel**

**PERIOD:** September 2019 - July 2020

**WP LEADER:** UU- Uppsala University, DU- Dagon University

**AIMS:** The ultimate aim of this WP is the implementation of international relations offices/units in the MM partner universities.

**TEAM AND PERSONNEL:** CHINLONE Consortium

# WP 4 –CHINLONE IR PLATFORM

## Activities

Activities		Personnel
No.	Title	
1	Workshop on mobility schemes and services at MoE. Full endorsement from the MoE to the implementation of new IROs	Consortium Partners and representatives of Country Universities
2	Study Visits to EU partners International Relations Office and dedicated facilities	Consortium Partners
3	Cascade trainings for spillover effect on International relations management and mobility services	MM partners
4	Drafting of the feasibility plans to implement IROs	MM partners
5	Implementation of IR offices at MM partners	MM partners

Part 2 – Workplan

## **WP 5 –DISSEMINATION**

### **Timeframe - Aim - Personnel**

**PERIOD:** During the entire duration of the project

**WP LEADER:** UGR- University of Granada, YAU- Yezin Agricultural University

**AIMS:** to maximize the spread and dissemination of the project's results both within and beyond MM, while building a lasting bridge between the country's HEIs and the local civil society

**TEAM AND PERSONNEL:** CHINLONE Consortium

# WP 5 – DISSEMINATION Activities

Activities		Personnel
No.	Title	
1	Project's website and social networks' profiles;	Consortium
2	New institutional promotional materials for MM Universities;	Consortium
3	Improvement of MM University websites;	Consortium
4	Improvement of degree courses website pages;	Consortium
5	Organization of University open days;	Consortium
6	Organization of IRO open days.	Consortium



## **WP 6 – EXPLOITATION**

### **Timeframe - Aim - Personnel**

**PERIOD:** 15 January 2020- 15 October 2020

**WP LEADER:** CG- Coimbra Group, MoE- Ministry of Education

**AIMS:** engaging the international community so to receive its feedbacks with respect to the project's methodology and approach, while exploring the feasibility of future implementations of the 'CHINLONE blueprint' also to other countries

**TEAM AND PERSONNEL:** CHINLONE Consortium

# WP 6 – CHINLONE EXPLOITATION

## Activities

Activities		Personnel
No.	Title	
1	Report on CHINLONE's project methodology to be used for other projects in transition countries	Consortium
2	Presentation of the CHINLONE's model to international conferences	Consortium
3	Establishment of students networks and alumni associations in MM	Consortium

## **WP 7 – QUALITY**

### **Timeframe - Aim - Personnel**

**PERIOD:** During the entire duration of the project

**WP LEADER:** UU- Uppsala University, YUEco- Yangon University of Economics

**AIMS:** To monitor and evaluate the quality of the project scientific outputs and deliverables. To monitor and evaluate the quality of project cooperation mechanism and administrative management. To monitor the degree of satisfaction of participants, users and target groups and to measure the impact of the project on the country.

**TEAM AND PERSONNEL:** CHINLONE Consortium

## WP 7 – QUALITY Activities

Activities		Personnel
No.	Title	
1	Internal Formative Evaluation (IFE)	Consortium
2	External Formative Evaluation (EFE)	Consortium
3	Internal Summative Evaluation (ISE)	Consortium
4	External Summative Evaluation (ISE)	Consortium

## **WP 8 – PROJECT MANAGEMENT**

### **Timeframe - Aim - Personnel**

**PERIOD:** During the entire duration of the project

**WP LEADER:** UNIBO - University of Bologna

**AIMS:** To guarantee a positive commencement, an uneventful implementation and a successful conclusion of the project; To set up an efficient and cost effective communication strategy among project partners including a clear and well defined decision making process; To coordinate the overall project management and financial administration

**TEAM AND PERSONNEL:** CHINLONE Consortium

# WP 8 – PROJECT MANAGEMENT

## Activities

Activities		Personnel
No.	Title	
1	Organization of the Consortium Assembly meetings	Consortium
2	Organization of Steering Committee meetings	Consortium
3	Overall management of the project and financial administration	Consortium

**Thank you for your attention**

Contacts

Ms. Franca Maria Mura and Ms. Licia Proserpio

CHINLONE COORDINATION TEAM

E-mail address: [diri.chinlone@unibo.it](mailto:diri.chinlone@unibo.it)
